
Plaid v1 — Plan Checklist (solver, edge-all)

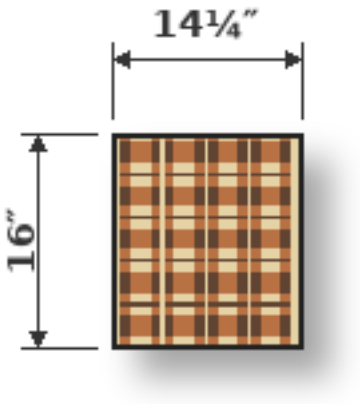


Phase 1 — Buy Wood

⚠ *Before getting started you should buy wood.*

	Board	Species	Length	Width	Thickness	Yields
☐	GH-C	Cherry	38⅞″	15⁄16″	13⁄16″	¾″ → 19⅜″x2

Phase 2 — Initial crosscuts ⚠

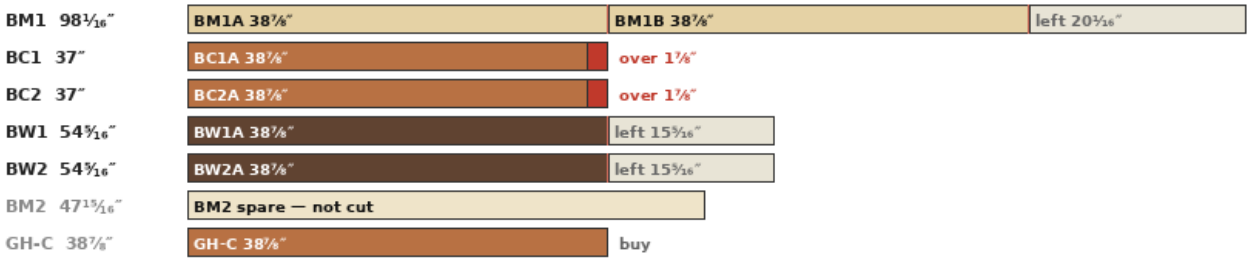

	Raw board	Species	Blank	Length	Off Cut
☐	BM1 (98 1⁄16″)	Brown Maple	BM1A	38⅞″	59 1⁄16″
☐	BM1 ↩	Brown Maple	BM1B	38⅞″	20 1⁄16″
☐	BC1 (37″)	Cherry	BC1A	38⅞″	-1⅞″ ⚠
☐	BC2 (37″)	Cherry	BC2A	38⅞″	-1⅞″ ⚠
☐	BW1 (54 5⁄16″)	Walnut	BW1A	38⅞″	15 5⁄16″
☐	BW2 (54 5⁄16″)	Walnut	BW2A	38⅞″	15 5⁄16″

Spare — do not cut: BM2 (Brown Maple, 47 15⁄16″).

⚠ *ERROR — Crosscut overflow: Board BC1 is over-cut by 1⅞″: its blanks demand more length than the raw board has.*

⚠ *ERROR — Crosscut overflow: Board BC2 is over-cut by 1⅞″: its blanks demand more length than the raw board has.*

Phase 3 — Rips

Phase 3.1 — BM1A — Brown Maple ⚠

BM1A (38⅞″ x 6″ x 13⁄16″)




	Rip	Rip size	Final width	Length	Pieces planned	Margin
☐	1	1⁹⁄16″ (1.56″)	1½″ (1.50″)	38⅞″	19⅜″x2	4⁵⁄16″
☐	2	1⁹⁄16″ (1.56″)	1½″ (1.50″)	38⅞″	19⅜″x2	2⅝″
☐	3	1⁹⁄16″ (1.56″)	1½″ (1.50″)	38⅞″	19⅜″x2	¹⁵⁄16″
☐	4	1⁹⁄16″ (1.56″)	1½″ (1.50″)	38⅞″	19⅜″x2	-¾″ ⚠
☐	5	¹³⁄16″ (0.81″)	¾″ (0.75″)	38⅞″	19⅜″x2	-1¹¹⁄16″ ⚠
☐	6	⁵⁄16″ (0.31″)	¼″ (0.25″)	38⅞″	19⅜″x2	-2⅛″ ⚠

Board width 6″ = used 7″ + loss 1⅛″ + margin -2⅛″ ⚠.

⚠ *ERROR — Over-rip: Cut list for board BM1A over-rips by 2⅛″: the strips are wider than the board.*

Phase 3.2 — BM1B — Brown Maple

BM1B (38⅞″ x 6″ x 13⁄16″)



	Rip	Rip size	Final width	Length	Pieces planned	Margin
☐	1	¹³⁄16″ (0.81″)	¾″ (0.75″)	38⅞″	19⅜″x2	5¹⁄16″
☐	2	¹³⁄16″ (0.81″)	¾″ (0.75″)	38⅞″	19⅜″x2	4⅛″
☐	3	¹³⁄16″ (0.81″)	¾″ (0.75″)	38⅞″	19⅜″x2	3³⁄16″

Board width 6″ = used 2¼″ + loss ⁹⁄16″ + margin 3³⁄16″.

Margin crosscuts — BM1B margin slab, length 38⅞″:

	Child blank	Length
☐	BM1B1	17¾″
☐	BM1B2	19⅜″

Rip the child boards next, in the order above, before the next parent board.

Phase 3.3 — BM1B1 — Brown Maple

BM1B1 (17¾″ x 3³⁄16″ x 13⁄16″)



	Rip	Rip size	Final width	Length	Pieces planned	Margin
☐	1	¹³⁄16″ (0.81″)	¾″ (0.75″)	17¾″	17¾″	2¼″
☐	2	⁵⁄16″ (0.31″)	¼″ (0.25″)	17¾″	17¾″	1¹³⁄16″
☐	3	⁵⁄16″ (0.31″)	¼″ (0.25″)	17¾″	17¾″	1⅜″

Board width 3 3/16″ = used 1 1/4″ + loss 9/16″ + margin 1 3/8″.

Phase 3.4 — BM1B2 — Brown Maple ⚠

BM1B2 (19 3/8″ x 3 3/16″ x 13/16″)



	Rip	Rip size	Final width	Length	Pieces planned	Margin
☐	1	5/16″ (0.31″)	1/4″ (0.25″)	19 3/8″	19 3/8″	2 3/4″
☐	2	5/16″ (0.31″)	1/4″ (0.25″)	19 3/8″	19 3/8″	2 5/16″
☐	3	5/16″ (0.31″)	1/4″ (0.25″)	19 3/8″	19 3/8″	1 7/8″
☐	4	5/16″ (0.31″)	1/4″ (0.25″)	19 3/8″	19 3/8″	1 7/16″
☐	5	5/16″ (0.31″)	1/4″ (0.25″)	19 3/8″	19 3/8″	1″
☐	6	5/16″ (0.31″)	1/4″ (0.25″)	19 3/8″	19 3/8″	9/16″
☐	7	5/16″ (0.31″)	1/4″ (0.25″)	19 3/8″	19 3/8″	1/8″
☐	8	5/16″ (0.31″)	1/4″ (0.25″)	19 3/8″	19 3/8″	-5/16″ ⚠
☐	9	5/16″ (0.31″)	1/4″ (0.25″)	19 3/8″	19 3/8″	-3/4″ ⚠
☐	10	5/16″ (0.31″)	1/4″ (0.25″)	19 3/8″	19 3/8″	-1 3/16″ ⚠

Board width 3 3/16″ = used 2 1/2″ + loss 1 7/8″ + margin -1 3/16″ ⚠.

⚠ *ERROR — Over-rip: Cut list for board BM1B2 over-rips by 1 3/16″: the strips are wider than the board.*

Phase 3.5 — BC1A — Cherry

BC1A (38 7/8″ x 7 3/16″ x 13/16″)



	Rip	Rip size	Final width	Length	Pieces planned	Margin
☐	1	1 9/16″ (1.56″)	1 1/2″ (1.50″)	38 7/8″	19 3/8″x2	5 1/2″
☐	2	1 9/16″ (1.56″)	1 1/2″ (1.50″)	38 7/8″	19 3/8″x2	3 13/16″
☐	3	1 9/16″ (1.56″)	1 1/2″ (1.50″)	38 7/8″	19 3/8″x2	2 1/8″
☐	4	13/16″ (0.81″)	3/4″ (0.75″)	38 7/8″	19 3/8″x2	1 3/16″
☐	5	13/16″ (0.81″)	3/4″ (0.75″)	38 7/8″	19 3/8″x2	1/4″

Board width 7 3/16″ = used 6″ + loss 15/16″ + margin 1/4″.

Phase 3.6 — BC2A — Cherry

BC2A (38 7/8″ x 6 1/2″ x 13/16″)



	Rip	Rip size	Final width	Length	Pieces planned	Margin
☐	1	1 9/16″ (1.56″)	1 1/2″ (1.50″)	38 7/8″	19 3/8″x2	4 13/16″

	Rip	Rip size	Final width	Length	Pieces planned	Margin
☐	2	13⁄16″ (0.81″)	¾″ (0.75″)	38⅞″	19⅜″x2	3⅞″
☐	3	13⁄16″ (0.81″)	¾″ (0.75″)	38⅞″	19⅜″x2	2 15⁄16″
☐	4	13⁄16″ (0.81″)	¾″ (0.75″)	38⅞″	19⅜″x2	2″
☐	5	13⁄16″ (0.81″)	¾″ (0.75″)	38⅞″	19⅜″x2	1 1⁄16″
☐	6	13⁄16″ (0.81″)	¾″ (0.75″)	38⅞″	19⅜″x2	⅛″

Board width 6½″ = used 5¼″ + loss 1⅛″ + margin ⅛″.

⚠ *WARNING — Small margin: Board BC2A leaves only ⅛″ margin (< ¼″) — too tight; prone to under-supplying strips if the board runs narrow.*

Phase 3.7 — GH-C — Cherry

GH-C (38⅞″ x 15⁄16″)



	Rip	Rip size	Final width	Length	Pieces planned	Margin
☐	1	13⁄16″ (0.81″)	¾″ (0.75″)	38⅞″	19⅜″x2	0″ ⚠

Board width 15⁄16″ = used ¾″ + loss 3⁄16″ + margin 0″ ⚠.

Phase 3.8 — BW1A — Walnut

BW1A (38⅞″ x 6¼″ x 13⁄16″)



	Rip	Rip size	Final width	Length	Pieces planned	Margin
☐	1	3 1⁄16″ (3.06″)	3″ (3.00″)*	38⅞″	17¾″x2	3 1⁄16″
☐	2	13⁄16″ (0.81″)	¾″ (0.75″)	38⅞″	19⅜″x2	2⅛″
☐	3	13⁄16″ (0.81″)	¾″ (0.75″)	38⅞″	19⅜″x2	1 3⁄16″
☐	4	13⁄16″ (0.81″)	¾″ (0.75″)	38⅞″	19⅜″x2	¼″

Board width 6¼″ = used 5¼″ + loss ¾″ + margin ¼″.

Phase 3.9 — BW2A — Walnut

BW2A (38⅞″ x 6 1⁄16″ x 13⁄16″)



	Rip	Rip size	Final width	Length	Pieces planned	Margin
☐	1	13⁄16″ (0.81″)	¾″ (0.75″)	38⅞″	19⅜″x2	5⅛″
☐	2	13⁄16″ (0.81″)	¾″ (0.75″)	38⅞″	19⅜″x2	4 3⁄16″
☐	3	13⁄16″ (0.81″)	¾″ (0.75″)	38⅞″	19⅜″x2	3¼″
☐	4	13⁄16″ (0.81″)	¾″ (0.75″)	38⅞″	19⅜″x2	2 5⁄16″

	Rip	Rip size	Final width	Length	Pieces planned	Margin
☐	5	13⁄16″ (0.81″)	¾″ (0.75″)	38⅞″	19⅜″x2	1⅜″

Board width 6 1⁄16″ = used 3¾″ + loss 15⁄16″ + margin 1⅜″.

Phase 4 — Plane by width

Phase 4.1 — Gang — Plane to 3″ — planer setting 3″ (2 components) — requires a gang

WARNING — There aren't enough 3″ strips to gang together to safely pass through the planer without tipping over. You might need sacrificial wood to tape onto it in order to prevent movement.

Crosscut first:

Cuts	Board	Strip	Species	Pieces	Off Cut
☐☐	BW1A	1	Walnut	17¾″x2	3⅛″

Plane as gang:

	Species	Count
☐	Walnut	2 components

Phase 4.2 — Gang — Plane to 1½″ — planer setting 1½″ (8 strips) — requires a gang

Requires a gang — tape strips together; total thickness 6½″ ≥ 1½″.

	Species	Count
☐	Brown Maple	4 strips
☐	Cherry	4 strips

Phase 4.3 — Gang — Plane to ¾″ — planer setting ¾″ (21 strips)

	Species	Count
☐	Brown Maple	5 strips
☐	Cherry	8 strips
☐	Walnut	8 strips

Phase 4.4 — Gang — Plane to ¼″ — planer setting ¼″ (13 strips)

	Species	Count
☐	Brown Maple	13 strips

Phase 5 — Crosscut components

Phase 5.1 — Crosscut grouping — by length

Length	Species	Final width	Pieces
17¾″	Brown Maple	¾″ (0.75″)	1
17¾″	Brown Maple	¼″ (0.25″)	2
19⅜″	Brown Maple	1½″ (1.50″)	8
19⅜″	Brown Maple	¾″ (0.75″)	8
19⅜″	Brown Maple	¼″ (0.25″)	12
19⅜″	Cherry	1½″ (1.50″)	8
19⅜″	Cherry	¾″ (0.75″)	16
19⅜″	Walnut	¾″ (0.75″)	16

Totals: 17¾″ ×3, 19⅜″ ×68.

Phase 5.2 — BM1A — Brown Maple

Cuts	Strip	Species	Final width	Pieces	Off Cut
☐☐	1	Brown Maple	1½″ (1.50″)	19⅜″x2	0″ ⚠
☐☐	2	Brown Maple	1½″ (1.50″)	19⅜″x2	0″ ⚠
☐☐	3	Brown Maple	1½″ (1.50″)	19⅜″x2	0″ ⚠
☐☐	4	Brown Maple	1½″ (1.50″)	19⅜″x2	0″ ⚠
☐☐	5	Brown Maple	¾″ (0.75″)	19⅜″x2	0″ ⚠
☐☐	6	Brown Maple	¼″ (0.25″)	19⅜″x2	0″ ⚠

Phase 5.3 — BM1B — Brown Maple

Cuts	Strip	Species	Final width	Pieces	Off Cut
☐☐	1	Brown Maple	¾″ (0.75″)	19⅜″x2	0″ ⚠
☐☐	2	Brown Maple	¾″ (0.75″)	19⅜″x2	0″ ⚠
☐☐	3	Brown Maple	¾″ (0.75″)	19⅜″x2	0″ ⚠

Phase 5.4 — BM1B1 — Brown Maple

Cuts	Strip	Species	Final width	Pieces	Off Cut
☐	1	Brown Maple	¾″ (0.75″)	17¾″	0″ ⚠
☐	2	Brown Maple	¼″ (0.25″)	17¾″	0″ ⚠
☐	3	Brown Maple	¼″ (0.25″)	17¾″	0″ ⚠

Phase 5.5 — BM1B2 — Brown Maple

Cuts	Strip	Species	Final width	Pieces	Off Cut
☐	1	Brown Maple	¼″ (0.25″)	19⅜″	0″ ⚠
☐	2	Brown Maple	¼″ (0.25″)	19⅜″	0″ ⚠
☐	3	Brown Maple	¼″ (0.25″)	19⅜″	0″ ⚠
☐	4	Brown Maple	¼″ (0.25″)	19⅜″	0″ ⚠
☐	5	Brown Maple	¼″ (0.25″)	19⅜″	0″ ⚠
☐	6	Brown Maple	¼″ (0.25″)	19⅜″	0″ ⚠
☐	7	Brown Maple	¼″ (0.25″)	19⅜″	0″ ⚠
☐	8	Brown Maple	¼″ (0.25″)	19⅜″	0″ ⚠
☐	9	Brown Maple	¼″ (0.25″)	19⅜″	0″ ⚠
☐	10	Brown Maple	¼″ (0.25″)	19⅜″	0″ ⚠

Phase 5.6 — BC1A — Cherry

Cuts	Strip	Species	Final width	Pieces	Off Cut
☐☐	1	Cherry	1½″ (1.50″)	19⅜″x2	0″ ⚠
☐☐	2	Cherry	1½″ (1.50″)	19⅜″x2	0″ ⚠
☐☐	3	Cherry	1½″ (1.50″)	19⅜″x2	0″ ⚠
☐☐	4	Cherry	¾″ (0.75″)	19⅜″x2	0″ ⚠
☐☐	5	Cherry	¾″ (0.75″)	19⅜″x2	0″ ⚠

Phase 5.7 — BC2A — Cherry

Cuts	Strip	Species	Final width	Pieces	Off Cut
☐☐	1	Cherry	1½″ (1.50″)	19⅜″x2	0″ ⚠
☐☐	2	Cherry	¾″ (0.75″)	19⅜″x2	0″ ⚠
☐☐	3	Cherry	¾″ (0.75″)	19⅜″x2	0″ ⚠
☐☐	4	Cherry	¾″ (0.75″)	19⅜″x2	0″ ⚠
☐☐	5	Cherry	¾″ (0.75″)	19⅜″x2	0″ ⚠
☐☐	6	Cherry	¾″ (0.75″)	19⅜″x2	0″ ⚠

Phase 5.8 — GH-C — Cherry

Cuts	Strip	Species	Final width	Pieces	Off Cut
☐☐	1	Cherry	¾″ (0.75″)	19⅜″x2	0″ ⚠

Phase 5.9 — BW1A — Walnut

Cuts	Strip	Species	Final width	Pieces	Off Cut
☐☐	2	Walnut	¾″ (0.75″)	19⅜″x2	0″ ⚠
☐☐	3	Walnut	¾″ (0.75″)	19⅜″x2	0″ ⚠
☐☐	4	Walnut	¾″ (0.75″)	19⅜″x2	0″ ⚠

Strip 1 (3″) already crosscut in Phase 4 gang, not repeated here.

Phase 5.10 — BW2A — Walnut

Cuts	Strip	Species	Final width	Pieces	Off Cut
☐☐	1	Walnut	¾″ (0.75″)	19⅜″x2	0″ ⚠
☐☐	2	Walnut	¾″ (0.75″)	19⅜″x2	0″ ⚠
☐☐	3	Walnut	¾″ (0.75″)	19⅜″x2	0″ ⚠
☐☐	4	Walnut	¾″ (0.75″)	19⅜″x2	0″ ⚠
☐☐	5	Walnut	¾″ (0.75″)	19⅜″x2	0″ ⚠

Total: 43 strips, 73 component pieces. (2 pieces crosscut in Phase 4 gang, not repeated in Phase 5.)

Phase 6 — Panel glue-ups

Phase 6.1 — Panel SL x2

19⅜″ x 7¼″ x ¾″ - 9 components - x2 duplicates

Panels	Order	Species	Width	Component
☐☐	1	Brown Maple	¾″ (0.75″)	Me
☐☐	2	Cherry	¾″ (0.75″)	C2
☐☐	3	Brown Maple	1½″ (1.50″)	M1
☐☐	4	Cherry	¾″ (0.75″)	C2
☐☐	5	Brown Maple	¼″ (0.25″)	Md
☐☐	6	Cherry	¾″ (0.75″)	C2
☐☐	7	Brown Maple	1½″ (1.50″)	M1
☐☐	8	Cherry	¾″ (0.75″)	C2
☐☐	9	Brown Maple	¼″ (0.25″)	Md

Phase 6.2 — Panel SR x2

19⅜″ x 7″ x ¾″ - 8 components - x2 duplicates

Panels	Order	Species	Width	Component
☐☐	1	Brown Maple	¾″ (0.75″)	Me
☐☐	2	Cherry	¾″ (0.75″)	C2
☐☐	3	Brown Maple	1½″ (1.50″)	M1
☐☐	4	Cherry	¾″ (0.75″)	C2
☐☐	5	Brown Maple	¼″ (0.25″)	Md
☐☐	6	Cherry	¾″ (0.75″)	C2

Panels	Order	Species	Width	Component
☐☐	7	Brown Maple	1½″ (1.50″)	M1
☐☐	8	Cherry	¾″ (0.75″)	C2

Phase 6.3 — Panel ML x2

19⅜″ x 7¼″ x ¾″ - 9 components - x2 duplicates

Panels	Order	Species	Width	Component
☐☐	1	Brown Maple	¾″ (0.75″)	Me
☐☐	2	Walnut	¾″ (0.75″)	W2
☐☐	3	Cherry	1½″ (1.50″)	C1
☐☐	4	Walnut	¾″ (0.75″)	W2
☐☐	5	Brown Maple	¼″ (0.25″)	Md
☐☐	6	Walnut	¾″ (0.75″)	W2
☐☐	7	Cherry	1½″ (1.50″)	C1
☐☐	8	Walnut	¾″ (0.75″)	W2
☐☐	9	Brown Maple	¼″ (0.25″)	Md

Phase 6.4 — Panel MR x2

19⅜″ x 7″ x ¾″ - 8 components - x2 duplicates

Panels	Order	Species	Width	Component
☐☐	1	Brown Maple	¾″ (0.75″)	Me
☐☐	2	Walnut	¾″ (0.75″)	W2
☐☐	3	Cherry	1½″ (1.50″)	C1
☐☐	4	Walnut	¾″ (0.75″)	W2
☐☐	5	Brown Maple	¼″ (0.25″)	Md
☐☐	6	Walnut	¾″ (0.75″)	W2
☐☐	7	Cherry	1½″ (1.50″)	C1
☐☐	8	Walnut	¾″ (0.75″)	W2

Phase 6.5 — Panel H

17¾″ x 7¼″ x ¼″ - 5 components - x1 duplicates

Panels	Order	Species	Width	Component
☐	1	Brown Maple	¾″ (0.75″)	Me
☐	2	Walnut	3″ (3.00″)	W1
☐	3	Brown Maple	¼″ (0.25″)	Md
☐	4	Walnut	3″ (3.00″)	W1
☐	5	Brown Maple	¼″ (0.25″)	Md

Phase 7 — Slices


1¾″ thick (1½″ after flattening)

	Slice	From panel	Slice Count
☐	SL	SL	11 x 2 = 22
☐	SR	SR	11 x 2 = 22
☐	ML	ML	11 x 2 = 22
☐	MR	MR	11 x 2 = 22
☐	H-L	H	5 x 2 = 10
☐	H-R	H	5 x 2 = 10

Phase 8 — Slice rips

	Slice	Rip to	Count
☐	H-L	¼″	10
☐	H-R	¼″	10

Phase 9 — Column Glue Ups

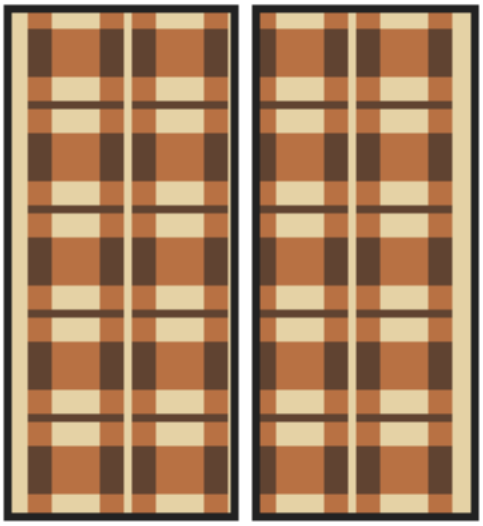

Board	Column	Slices
☐☐	Column 1	01 ☐SL 02 ☐ML 03 ☐ML 04 ☐SL 05 ☐H-L 06 ☐SL 07 ☐ML 08 ☐ML 09 ☐SL 10 ☐H-L 11 ☐SL 12 ☐ML 13 ☐ML 14 ☐SL 15 ☐H-L 16 ☐SL 17 ☐ML 18 ☐ML 19 ☐SL 20 ☐H-L 21 ☐SL 22 ☐ML 23 ☐ML 24 ☐SL
☐☐	Column 2	01 ☐SR* 02 ☐MR* 03 ☐MR* 04 ☐SR* 05 ☐H-R* 06 ☐SR* 07 ☐MR* 08 ☐MR* 09 ☐SR* 10 ☐H-R* 11 ☐SR* 12 ☐MR* 13 ☐MR* 14 ☐SR* 15 ☐H-R* 16 ☐SR* 17 ☐MR* 18 ☐MR* 19 ☐SR* 20 ☐H-R* 21 ☐SR* 22 ☐MR* 23 ☐MR* 24 ☐SR*

Phase 10 — Final Glue Up

Board	Columns	Size
☐	Column 1 + Column 2	14¼″ × 16″ × 1½″
☐	Column 1 + Column 2	14¼″ × 16″ × 1½″

Phase 11 — Finishing

Final dimensions: 14″ × 16″ × 1¼″

Board	Width trim	Length trim	Flatten	Sanding (grits)	Oil	Wax
☐	14¼″ → 14″	16″ → 16″	1½″ → 1¼″	☐80 ☐120 ☐220 ☐320	☐	☐
☐	14¼″ → 14″	16″ → 16″	1½″ → 1¼″	☐80 ☐120 ☐220 ☐320	☐	☐
