

Plaid v1 — Plan Checklist (hand, actual)

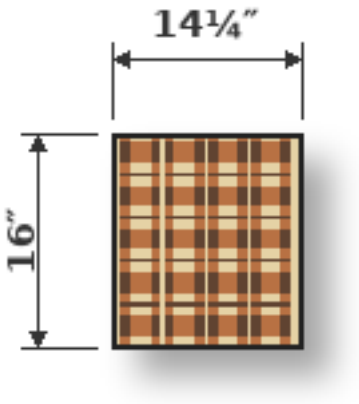

Phase 1 — Initial crosscuts ⚠



	Raw board	Species	Blank	Length	Off Cut
☐	BM1 (98¹⁄₁₆″)	Brown Maple	BM1A	48″	49¹⁵⁄₁₆″
☐	BM1 ↩	Brown Maple	BM1B	48″	1¹³⁄₁₆″
☐	BC1 (48¹⁄₁₆″)	Cherry	BC1A	48″	0″ ⚠
☐	BC2 (48¹⁄₁₆″)	Cherry	BC2A	48″	0″ ⚠
☐	BW1 (54⁵⁄₁₆″)	Walnut	BW1A	48″	6³⁄₁₆″
☐	BW2 (54⁵⁄₁₆″)	Walnut	BW2A	48″	6³⁄₁₆″

Spare — do not cut: BM2 (Brown Maple, 47¹⁵⁄₁₆″).

⚠ *WARNING — Board BC1's cut is close to the end of the board, so the saw blade will be shaving off the end with no off cut.*

⚠ *WARNING — Board BC2's cut is close to the end of the board, so the saw blade will be shaving off the end with no off cut.*

Phase 2 — Rips

Phase 2.1 — BM1A — Brown Maple

BM1A (48″ x 8⁷⁄₁₆″ x ¹³⁄₁₆″)



	Rip	Rip size	Final width	Length	Pieces planned	Margin
☐	1	1⁹⁄₁₆″ (1.56″)	1½″ (1.50″)	48″	19⅜″x2	6¾″
☐	2	1⁹⁄₁₆″ (1.56″)	1½″ (1.50″)	48″	19⅜″x2	5¹⁄₁₆″

	Rip	Rip size	Final width	Length	Pieces planned	Margin
☐	3	1 9⁄16″ (1.56″)	1½″ (1.50″)	48″	19⅜″x2	3⅜″
☐	4	1 9⁄16″ (1.56″)	1½″ (1.50″)	48″	19⅜″x2	1 11⁄16″
☐	5	13⁄16″ (0.81″)	¾″ (0.75″)	48″	19⅜″x2	¾″
☐	6	5⁄16″ (0.31″)	¼″ (0.25″)	48″	19⅜″x2	5⁄16″

Board width 8 7⁄16″ = used 7″ + loss 1⅛″ + margin 5⁄16″.

Phase 2.2 — BM1B — Brown Maple

BM1B (48″ x 8 7⁄16″ x 13⁄16″)



	Rip	Rip size	Final width	Length	Pieces planned	Margin
☐	1	13⁄16″ (0.81″)	¾″ (0.75″)	48″	19⅜″x2	7½″
☐	2	13⁄16″ (0.81″)	¾″ (0.75″)	48″	19⅜″x2	6 9⁄16″
☐	3	13⁄16″ (0.81″)	¾″ (0.75″)	48″	19⅜″x2	5⅝″
☐	4	13⁄16″ (0.81″)	¾″ (0.75″)	48″	17¾″	4 11⁄16″
☐	5	5⁄16″ (0.31″)	¼″ (0.25″)	48″	19⅜″x2	4¼″
☐	6	5⁄16″ (0.31″)	¼″ (0.25″)	48″	19⅜″x2	3 13⁄16″
☐	7	5⁄16″ (0.31″)	¼″ (0.25″)	48″	19⅜″x2	3⅜″
☐	8	5⁄16″ (0.31″)	¼″ (0.25″)	48″	19⅜″x2	2 15⁄16″
☐	9	5⁄16″ (0.31″)	¼″ (0.25″)	48″	19⅜″x2	2½″
☐	10	5⁄16″ (0.31″)	¼″ (0.25″)	48″	17¾″x2	2 1⁄16″

Board width 8 7⁄16″ = used 4½″ + loss 1⅞″ + margin 2 1⁄16″.

Phase 2.3 — BC1A — Cherry ⚠

BC1A (48″ x 7 3⁄16″ x 13⁄16″)



	Rip	Rip size	Final width	Length	Pieces planned	Margin
☐	1	1 9⁄16″ (1.56″)	1½″ (1.50″)	48″	19⅜″x2	5½″
☐	2	13⁄16″ (0.81″)	¾″ (0.75″)	48″	19⅜″x2	4 9⁄16″
☐	3	13⁄16″ (0.81″)	¾″ (0.75″)	48″	19⅜″x2	3⅝″
☐	4	13⁄16″ (0.81″)	¾″ (0.75″)	48″	19⅜″x2	2 11⁄16″
☐	5	13⁄16″ (0.81″)	¾″ (0.75″)	48″	19⅜″x2	1¾″
☐	6	13⁄16″ (0.81″)	¾″ (0.75″)	48″	19⅜″x2	13⁄16″
☐	7	13⁄16″ (0.81″)	¾″ (0.75″)	48″	19⅜″x2	-⅛″ ⚠

Board width 7 3⁄16″ = used 6″ + loss 1 5⁄16″ + margin -⅛″ ⚠.

⚠ *ERROR — Over-rip: Cut list for board BC1A over-rips by ⅛″: the strips are wider than the board.*

Phase 2.4 — BC2A — Cherry ⚠

BC2A (48″ x 6½″ x 13⁄16″)



	Rip	Rip size	Final width	Length	Pieces planned	Margin
☐	1	1⁹⁄16″ (1.56″)	1½″ (1.50″)	48″	19⅜″x2	4¹³⁄16″
☐	2	1⁹⁄16″ (1.56″)	1½″ (1.50″)	48″	19⅜″x2	3⅛″
☐	3	1⁹⁄16″ (1.56″)	1½″ (1.50″)	48″	19⅜″x2	1⁷⁄16″
☐	4	¹³⁄16″ (0.81″)	¾″ (0.75″)	48″	19⅜″x2	½″
☐	5	¹³⁄16″ (0.81″)	¾″ (0.75″)	48″	19⅜″x2	-⁷⁄16″ ⚠

Board width 6½″ = used 6″ + loss ¹⁵⁄16″ + margin -⁷⁄16″ ⚠.

⚠ *ERROR — Over-rip: Cut list for board BC2A over-rips by ⁷⁄16″: the strips are wider than the board.*

Phase 2.5 — BW1A — Walnut

BW1A (48″ x 6¼″ x 13⁄16″)



	Rip	Rip size	Final width	Length	Pieces planned	Margin
☐	1	3¹⁄16″ (3.06″)	3″ (3.00″)*	48″	17¾″x2	3¹⁄16″
☐	2	¹³⁄16″ (0.81″)	¾″ (0.75″)	48″	19⅜″x2	2⅛″
☐	3	¹³⁄16″ (0.81″)	¾″ (0.75″)	48″	19⅜″x2	1³⁄16″
☐	4	¹³⁄16″ (0.81″)	¾″ (0.75″)	48″	19⅜″x2	¼″

Board width 6¼″ = used 5¼″ + loss ¾″ + margin ¼″.

Phase 2.6 — BW2A — Walnut

BW2A (48″ x 6¹⁄16″ x 13⁄16″)



	Rip	Rip size	Final width	Length	Pieces planned	Margin
☐	1	¹³⁄16″ (0.81″)	¾″ (0.75″)	48″	19⅜″x2	5⅛″
☐	2	¹³⁄16″ (0.81″)	¾″ (0.75″)	48″	19⅜″x2	4³⁄16″
☐	3	¹³⁄16″ (0.81″)	¾″ (0.75″)	48″	19⅜″x2	3¼″
☐	4	¹³⁄16″ (0.81″)	¾″ (0.75″)	48″	19⅜″x2	2⁵⁄16″
☐	5	¹³⁄16″ (0.81″)	¾″ (0.75″)	48″	19⅜″x2	1⅜″

Board width 6¹⁄16″ = used 3¾″ + loss ¹⁵⁄16″ + margin 1⅜″.

Phase 3 — Plane by width

Phase 3.1 — Gang — Plane to 3″ — planer setting 3″ (2 components) — requires a gang

WARNING — There aren't enough 3″ strips to gang together to safely pass through the planer without tipping over. You might need sacrificial wood to tape onto it in order to prevent movement.

Crosscut first:

Cuts	Board	Strip	Species	Pieces	Off Cut
☐☐	BW1A	1	Walnut	17¾″x2	12¼″

Plane as gang:

	Species	Count
☐	Walnut	2 components

Phase 3.2 — Gang — Plane to 1½″ — planer setting 1½″ (8 strips) — requires a gang

Requires a gang — tape strips together; total thickness 6½″ ≥ 1½″.

	Species	Count
☐	Brown Maple	4 strips
☐	Cherry	4 strips

Phase 3.3 — Gang — Plane to ¾″ — planer setting ¾″ (21 strips)

	Species	Count
☐	Brown Maple	5 strips
☐	Cherry	8 strips
☐	Walnut	8 strips

Phase 3.4 — Gang — Plane to ¼″ — planer setting ¼″ (7 strips)

	Species	Count
☐	Brown Maple	7 strips

Phase 4 — Crosscut components

Phase 4.1 — Crosscut grouping — by length

Length	Species	Final width	Pieces
17¾″	Brown Maple	¾″ (0.75″)	1
17¾″	Brown Maple	¼″ (0.25″)	2
19⅜″	Brown Maple	1½″ (1.50″)	8
19⅜″	Brown Maple	¾″ (0.75″)	8
19⅜″	Brown Maple	¼″ (0.25″)	12
19⅜″	Cherry	1½″ (1.50″)	8
19⅜″	Cherry	¾″ (0.75″)	16
19⅜″	Walnut	¾″ (0.75″)	16

Totals: 17¾″ ×3, 19⅜″ ×68.

Phase 4.2 — BM1A — Brown Maple

Cuts	Strip	Species	Final width	Pieces	Off Cut
☐☐	1	Brown Maple	1½″ (1.50″)	19⅜″x2	9″
☐☐	2	Brown Maple	1½″ (1.50″)	19⅜″x2	9″
☐☐	3	Brown Maple	1½″ (1.50″)	19⅜″x2	9″
☐☐	4	Brown Maple	1½″ (1.50″)	19⅜″x2	9″
☐☐	5	Brown Maple	¾″ (0.75″)	19⅜″x2	9″
☐☐	6	Brown Maple	¼″ (0.25″)	19⅜″x2	9″

Phase 4.3 — BM1B — Brown Maple

Cuts	Strip	Species	Final width	Pieces	Off Cut
☐☐	1	Brown Maple	¾″ (0.75″)	19⅜″x2	9″
☐☐	2	Brown Maple	¾″ (0.75″)	19⅜″x2	9″
☐☐	3	Brown Maple	¾″ (0.75″)	19⅜″x2	9″
☐	4	Brown Maple	¾″ (0.75″)	17¾″	30⅛″
☐☐	5	Brown Maple	¼″ (0.25″)	19⅜″x2	9″
☐☐	6	Brown Maple	¼″ (0.25″)	19⅜″x2	9″
☐☐	7	Brown Maple	¼″ (0.25″)	19⅜″x2	9″
☐☐	8	Brown Maple	¼″ (0.25″)	19⅜″x2	9″
☐☐	9	Brown Maple	¼″ (0.25″)	19⅜″x2	9″
☐☐	10	Brown Maple	¼″ (0.25″)	17¾″x2	12¼″

Phase 4.4 — BC1A — Cherry

Cuts	Strip	Species	Final width	Pieces	Off Cut
☐☐	1	Cherry	1½″ (1.50″)	19⅜″x2	9″
☐☐	2	Cherry	¾″ (0.75″)	19⅜″x2	9″
☐☐	3	Cherry	¾″ (0.75″)	19⅜″x2	9″
☐☐	4	Cherry	¾″ (0.75″)	19⅜″x2	9″
☐☐	5	Cherry	¾″ (0.75″)	19⅜″x2	9″
☐☐	6	Cherry	¾″ (0.75″)	19⅜″x2	9″
☐☐	7	Cherry	¾″ (0.75″)	19⅜″x2	9″

Phase 4.5 — BC2A — Cherry

Cuts	Strip	Species	Final width	Pieces	Off Cut
☐☐	1	Cherry	1½″ (1.50″)	19⅜″x2	9″
☐☐	2	Cherry	1½″ (1.50″)	19⅜″x2	9″
☐☐	3	Cherry	1½″ (1.50″)	19⅜″x2	9″
☐☐	4	Cherry	¾″ (0.75″)	19⅜″x2	9″
☐☐	5	Cherry	¾″ (0.75″)	19⅜″x2	9″

Phase 4.6 — BW1A — Walnut

Cuts	Strip	Species	Final width	Pieces	Off Cut
☐☐	2	Walnut	¾″ (0.75″)	19⅜″x2	9″
☐☐	3	Walnut	¾″ (0.75″)	19⅜″x2	9″
☐☐	4	Walnut	¾″ (0.75″)	19⅜″x2	9″

Strip 1 (3″) already crosscut in Phase 3 gang, not repeated here.

Phase 4.7 — BW2A — Walnut

Cuts	Strip	Species	Final width	Pieces	Off Cut
☐☐	1	Walnut	¾″ (0.75″)	19⅜″x2	9″
☐☐	2	Walnut	¾″ (0.75″)	19⅜″x2	9″
☐☐	3	Walnut	¾″ (0.75″)	19⅜″x2	9″
☐☐	4	Walnut	¾″ (0.75″)	19⅜″x2	9″
☐☐	5	Walnut	¾″ (0.75″)	19⅜″x2	9″

Total: 37 strips, 73 component pieces. (2 pieces crosscut in Phase 3 gang, not repeated in Phase 4.)

Phase 5 — Panel glue-ups

Phase 5.1 — Panel SL x2

19⅜″ x 7¼″ x ¾″ - 9 components - x2 duplicates

Panels	Order	Species	Width	Component
☐☐	1	Brown Maple	¾″ (0.75″)	Me
☐☐	2	Cherry	¾″ (0.75″)	C2
☐☐	3	Brown Maple	1½″ (1.50″)	M1
☐☐	4	Cherry	¾″ (0.75″)	C2
☐☐	5	Brown Maple	¼″ (0.25″)	Md
☐☐	6	Cherry	¾″ (0.75″)	C2
☐☐	7	Brown Maple	1½″ (1.50″)	M1
☐☐	8	Cherry	¾″ (0.75″)	C2
☐☐	9	Brown Maple	¼″ (0.25″)	Md

Phase 5.2 — Panel SR x2

19⅜″ x 7″ x ¾″ - 8 components - x2 duplicates

Panels	Order	Species	Width	Component
☐☐	1	Brown Maple	¾″ (0.75″)	Me
☐☐	2	Cherry	¾″ (0.75″)	C2
☐☐	3	Brown Maple	1½″ (1.50″)	M1
☐☐	4	Cherry	¾″ (0.75″)	C2
☐☐	5	Brown Maple	¼″ (0.25″)	Md
☐☐	6	Cherry	¾″ (0.75″)	C2
☐☐	7	Brown Maple	1½″ (1.50″)	M1
☐☐	8	Cherry	¾″ (0.75″)	C2

Phase 5.3 — Panel ML x2

19⅜″ x 7¼″ x ¾″ - 9 components - x2 duplicates

Panels	Order	Species	Width	Component
☐☐	1	Brown Maple	¾″ (0.75″)	Me
☐☐	2	Walnut	¾″ (0.75″)	W2
☐☐	3	Cherry	1½″ (1.50″)	C1
☐☐	4	Walnut	¾″ (0.75″)	W2
☐☐	5	Brown Maple	¼″ (0.25″)	Md
☐☐	6	Walnut	¾″ (0.75″)	W2
☐☐	7	Cherry	1½″ (1.50″)	C1
☐☐	8	Walnut	¾″ (0.75″)	W2
☐☐	9	Brown Maple	¼″ (0.25″)	Md

Phase 5.4 — Panel MR x2

19⅜″ x 7″ x ¾″ - 8 components - x2 duplicates

Panels	Order	Species	Width	Component
☐☐	1	Brown Maple	¾″ (0.75″)	Me
☐☐	2	Walnut	¾″ (0.75″)	W2
☐☐	3	Cherry	1½″ (1.50″)	C1
☐☐	4	Walnut	¾″ (0.75″)	W2
☐☐	5	Brown Maple	¼″ (0.25″)	Md
☐☐	6	Walnut	¾″ (0.75″)	W2
☐☐	7	Cherry	1½″ (1.50″)	C1
☐☐	8	Walnut	¾″ (0.75″)	W2

Phase 5.5 — Panel H

17¾″ x 7¼″ x ¼″ - 5 components - x1 duplicates

Panels	Order	Species	Width	Component
☐	1	Brown Maple	¾″ (0.75″)	Me
☐	2	Walnut	3″ (3.00″)	W1
☐	3	Brown Maple	¼″ (0.25″)	Md
☐	4	Walnut	3″ (3.00″)	W1
☐	5	Brown Maple	¼″ (0.25″)	Md

Phase 6 — Slices


1¾″ thick (1½″ after flattening)

	Slice	From panel	Slice Count
☐	SL	SL	11 x 2 = 22
☐	SR	SR	11 x 2 = 22
☐	ML	ML	11 x 2 = 22
☐	MR	MR	11 x 2 = 22
☐	H-L	H	5 x 2 = 10
☐	H-R	H	5 x 2 = 10

Phase 7 — Slice rips

	Slice	Rip to	Count
☐	H-L	¼″	10
☐	H-R	¼″	10

Phase 8 — Column Glue Ups

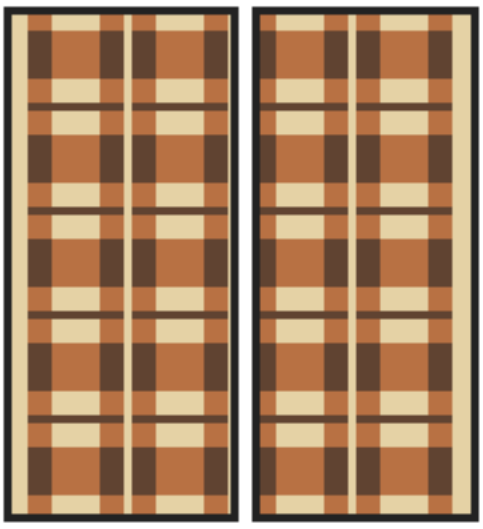

Board	Column	Slices
☐☐	Column 1	01 ☐SL 02 ☐ML 03 ☐ML 04 ☐SL 05 ☐H-L 06 ☐SL 07 ☐ML 08 ☐ML 09 ☐SL 10 ☐H-L 11 ☐SL 12 ☐ML 13 ☐ML 14 ☐SL 15 ☐H-L 16 ☐SL 17 ☐ML 18 ☐ML 19 ☐SL 20 ☐H-L 21 ☐SL 22 ☐ML 23 ☐ML 24 ☐SL
☐☐	Column 2	01 ☐SR* 02 ☐MR* 03 ☐MR* 04 ☐SR* 05 ☐H-R* 06 ☐SR* 07 ☐MR* 08 ☐MR* 09 ☐SR* 10 ☐H-R* 11 ☐SR* 12 ☐MR* 13 ☐MR* 14 ☐SR* 15 ☐H-R* 16 ☐SR* 17 ☐MR* 18 ☐MR* 19 ☐SR* 20 ☐H-R* 21 ☐SR* 22 ☐MR* 23 ☐MR* 24 ☐SR*

Phase 9 — Final Glue Up

Board	Columns	Size
☐	Column 1 + Column 2	14¼″ × 16″ × 1½″
☐	Column 1 + Column 2	14¼″ × 16″ × 1½″

Phase 10 — Finishing

Final dimensions: 14″ × 16″ × 1¼″

Board	Width trim	Length trim	Flatten	Sanding (grits)	Oil	Wax
☐	14¼″ → 14″	16″ → 16″	1½″ → 1¼″	☐80 ☐120 ☐220 ☐320	☐	☐
☐	14¼″ → 14″	16″ → 16″	1½″ → 1¼″	☐80 ☐120 ☐220 ☐320	☐	☐
